

# Piney Point



Last Updated: November 2024

## PROJECT DETAILS

### Project Numbers:

6107400  
6107480

[Capital Improvement Plan](#)

### Project Managers:

Anthony Benitez

## PROJECT HIGHLIGHTS AND COMMUNITY BENEFITS

Due to the leakage of waters contained in Piney Point phosphogypsum stacks, Manatee County Utilities crews began safe and secure disposal of those waters through a fully permitted injection well. The pre-treatment facility associated with Manatee County’s Underground Injection Control (UIC) well along Buckeye Road continues to treat the process water contained in the remaining compartment areas at the former Piney Point site.

## PROJECT SCHEDULE

### Design Start:

April 1, 2021

### Design End:

January 31, 2023

### Construction Start:

July 1, 2021


### Construction End:

March 31, 2024



## FINANCIAL STATUS

Appropriated to Date	\$32,937,816
Future Appropriation	\$0
Total Anticipated Costs	\$32,937,816
Funds Expended/ Spent to Date	\$32,226,358
Funds Remaining	\$711,458
Funding Strategy	General Revenue, Debt

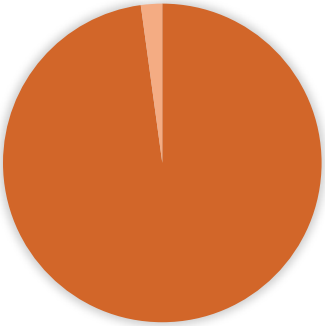

Funds Expended/  
Spent to Date:  
\$32,226,358  
(98%)

Funds  
Remaining:  
\$711,458  
(2%)
